


ID		Task Name	Duration	Start	Finish	13 Dec '09							20 Dec '09							27
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
1																				
2		Requirements	4 days?	Mon 21/12/09	Thu 24/12/09															
3		Requirements assets received	1 day?	Mon 21/12/09	Mon 21/12/09															
4		Requirements documentation written and finalised	2 days	Tue 22/12/09	Wed 23/12/09															
5		Requirements documentation signed off by client	1 day?	Thu 24/12/09	Thu 24/12/09															
6		System & DB Design	10 days	Tue 22/12/09	Mon 4/01/10															
7		Web Site Design and build	20 days?	Tue 22/12/09	Mon 18/01/10															
8		Design assets received (content reqts per page, logos, colour pa	0.5 days	Tue 22/12/09	Tue 22/12/09															
9		Home Page Design	1 day	Tue 22/12/09	Wed 23/12/09															
10		Navigation Flow Design	1 day	Wed 23/12/09	Thu 24/12/09															
11		Headers & Footers	0.5 days	Thu 24/12/09	Thu 24/12/09															
12		Internal Pages design with Page/Section Theme Headers	2 days	Mon 28/12/09	Tue 29/12/09															
13		Program Landing Page and Internal pages design	2 days	Wed 30/12/09	Thu 31/12/09															
14		Workflow Design Pages for Admin Section	1 day?	Fri 1/01/10	Fri 1/01/10															
15		Feedback received on design	3 days	Mon 4/01/10	Wed 6/01/10															
16		Design signed off by client	3 days	Thu 7/01/10	Mon 11/01/10															
17		Admin Section	5 days?	Tue 12/01/10	Mon 18/01/10															
18		User Management	1 day?	Tue 12/01/10	Tue 12/01/10															
19		Programs Management	1 day?	Wed 13/01/10	Wed 13/01/10															
20		Permissions Interface	1 day?	Thu 14/01/10	Thu 14/01/10															
21		Different Roles Login Management	1 day?	Fri 15/01/10	Fri 15/01/10															
22		My Account/Change Password	1 day?	Mon 18/01/10	Mon 18/01/10															
23		Admin interface design signed off by client	3 days	Tue 12/01/10	Thu 14/01/10															
24		Content Management System	10.5 days?	Tue 19/01/10	Tue 2/02/10															
25		Category Management	1 day	Tue 19/01/10	Tue 19/01/10															
26		Categories Listing	0.5 days	Wed 20/01/10	Wed 20/01/10															
27		Add/Edit/Delete Categories	1 day	Wed 20/01/10	Thu 21/01/10															
28		Enable/Disable Categories	1 day	Thu 21/01/10	Fri 22/01/10															
29		Sort Order of Categories	1 day	Fri 22/01/10	Mon 25/01/10															
30		Pages Management	1 day	Mon 25/01/10	Tue 26/01/10															
31		Pages Listing	1 day?	Tue 26/01/10	Wed 27/01/10															
32		Add/Edit Page	1 day?	Wed 27/01/10	Thu 28/01/10															
33		Integration of WYSIWYG Editor	2 days	Thu 28/01/10	Mon 1/02/10															
34		Enable/Disable/Delete Pages	0.5 days	Mon 1/02/10	Mon 1/02/10															
35		Sort order of pages	0.5 days	Tue 2/02/10	Tue 2/02/10															
36		Assets/Content added to website	3 days?	Tue 2/02/10	Fri 5/02/10															
37		Web content (images, copy etc) delivered by client	1 day?	Tue 2/02/10	Wed 3/02/10															
38		Web content inserted into page	3 days	Tue 2/02/10	Fri 5/02/10															
39		QA & Internal Testing	2.5 days	Tue 2/02/10	Thu 4/02/10															

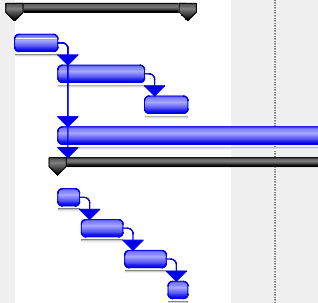

Project: ACELG_website_projectplan Date: Wed 16/12/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

Page 1

ID		Task Name	Duration	Start	Finish	13 Dec '09							20 Dec '09							27
						S	M	T	W	T	F	S	S	M	T	W	T	F	S	S
40		CMS Help Manual/Documentation	2 days	Tue 2/02/10	Thu 4/02/10															
41		User Acceptance Testing & Project Delivery	2 days	Fri 5/02/10	Mon 8/02/10															

Project: ACELG_website_projectplan
Date: Wed 16/12/09

Task



Milestone



External Tasks



Split



Summary



External Milestone



Progress




Project Summary



Deadline



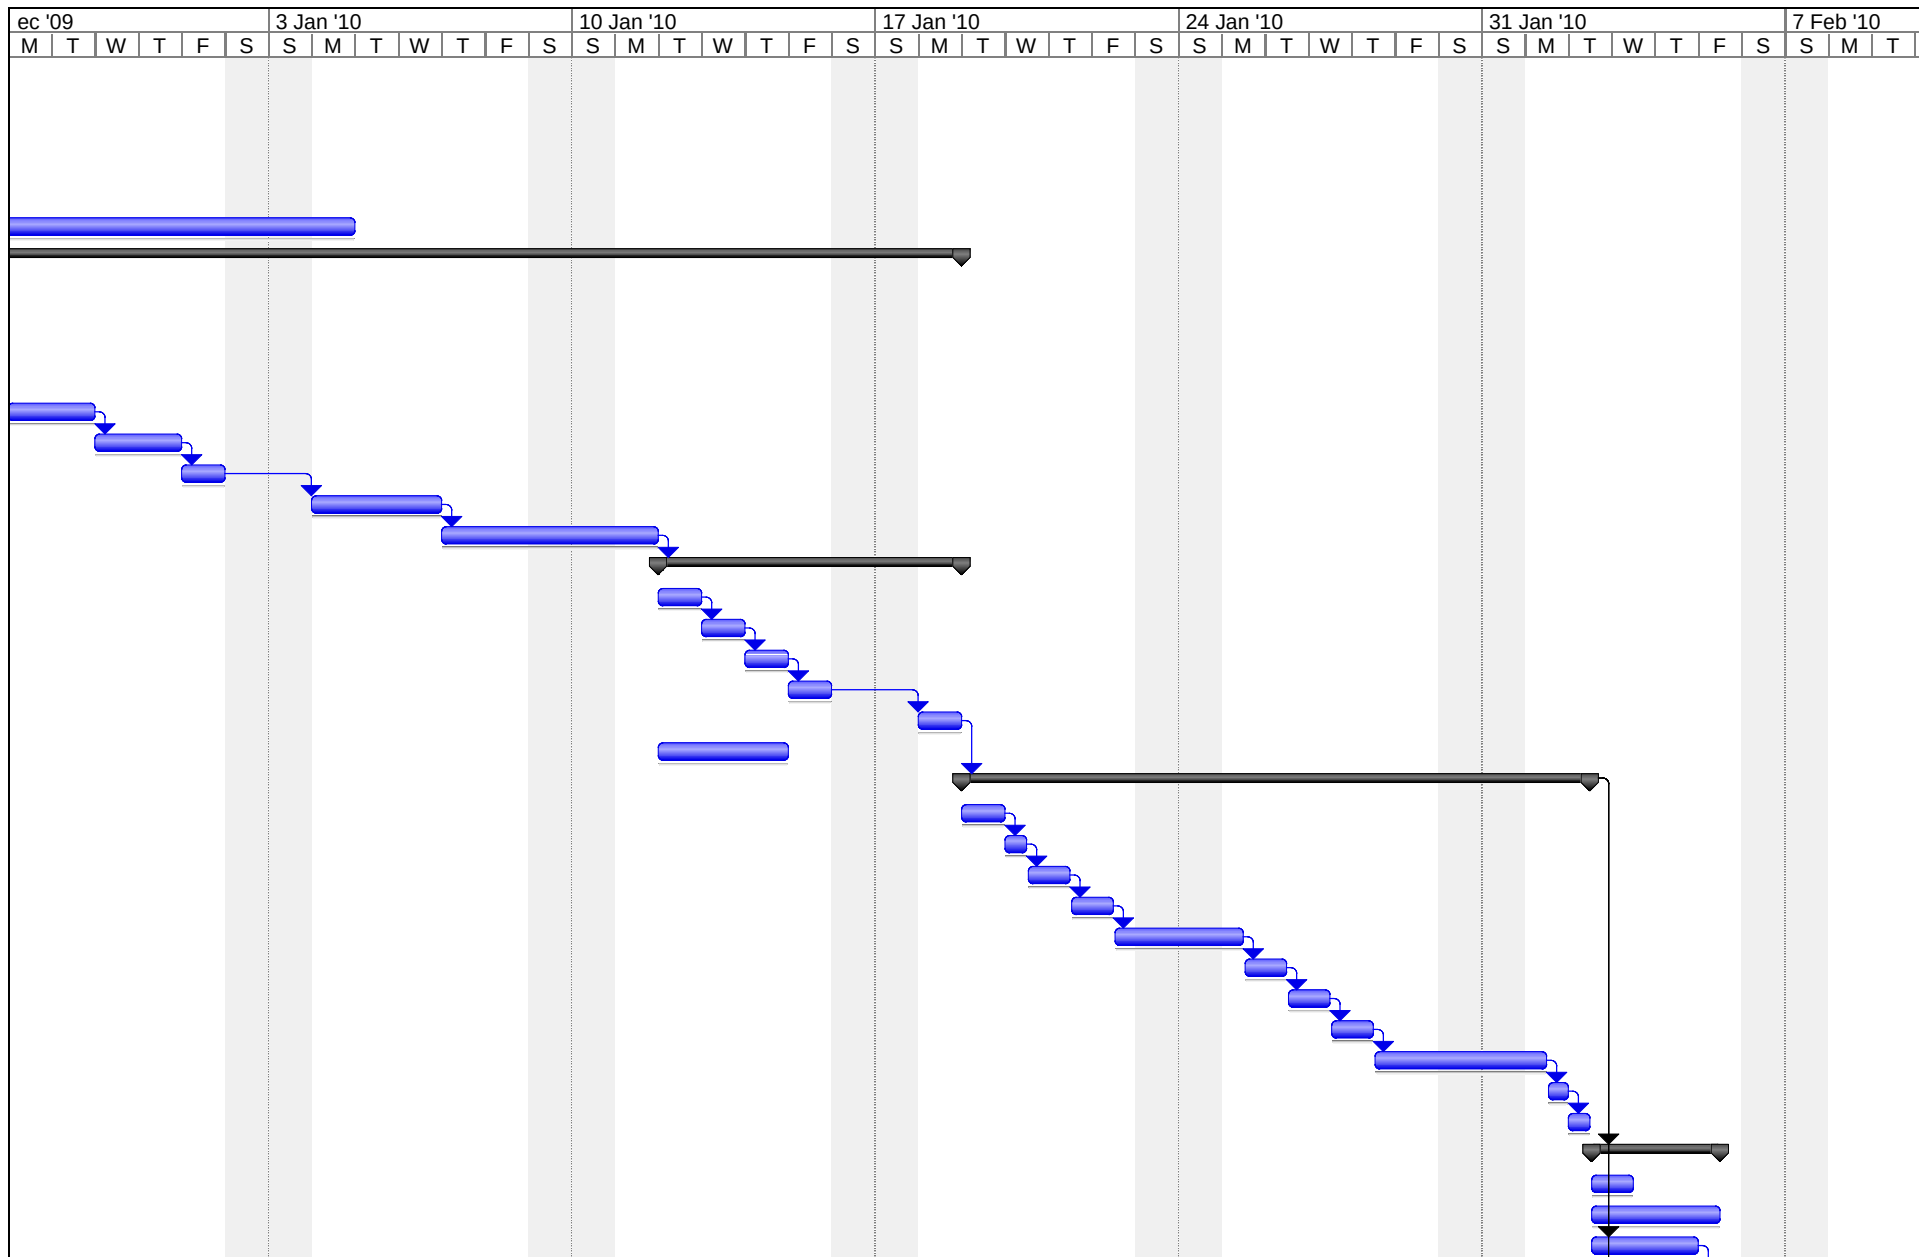

Project: ACELG_website_projectplan
Date: Wed 16/12/09

Task
Split
Progress

Milestone
Summary
Project Summary

External Tasks
External Milestone
Deadline

ec '09							3 Jan '10							10 Jan '10							17 Jan '10							24 Jan '10							31 Jan '10							7 Feb '10			
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T									



Project: ACELG_website_projectplan Date: Wed 16/12/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
